


City of Foley



Construction Project Update

April 2016



Cedar and Azalea Pipe Replacement + Ashland Court

Status: Closing Out

Engineer: COF

Contractor: Blade

Budgeted Cost: \$75,000



Cost to Date: \$ 74,173

Dog Park



Status:

Grass

Engineer:

COF

Contractor:

City Forces





Fairway Drive Turnout Improvement

Status: Begin Work 4/25

Engineer:

COF

Contractor:

R&S

Budgeted Cost: \$105,750



As-Bid: \$ 91,910

Graham Creek Estates Drainage Improvements



Status: Warranty Items

Engineer: Sawgrass

Contractor: Blade

Graham Creek Park Road Extension



Status: Phase II Permitted

Engineer: COF

Contractor: Public Works



North Pine Street Drainage Improvements



Status:

Punch List

Engineer:

HMR

Contractor:

BCC





Oak Street/Berry Avenue Drainage Improvements


Status: Driveways

Engineer: COF

Contractor: Public Works



Pride Drive ATRIP

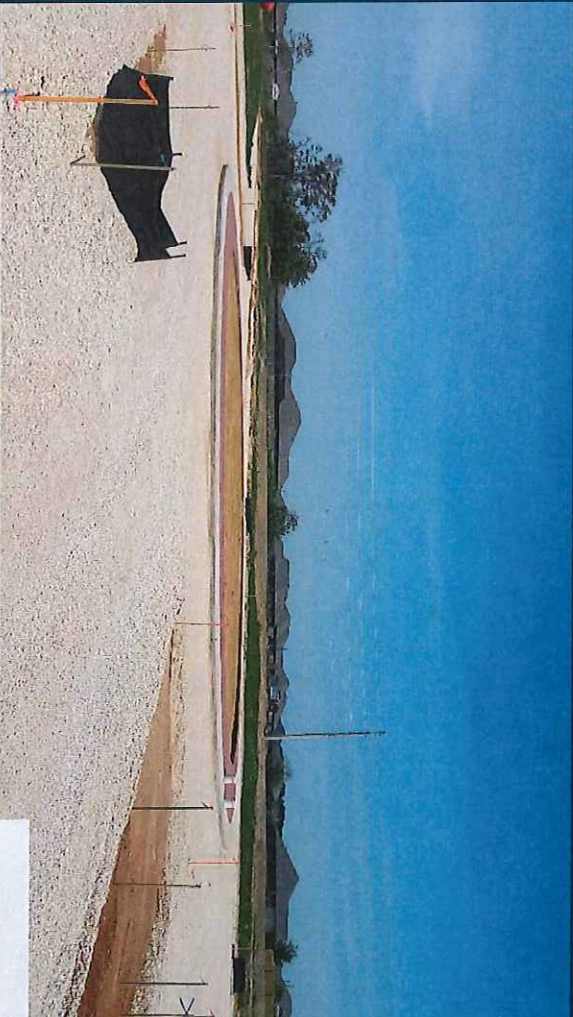

Status: Juniper/Curb
Engineer: Volkert
Contractor: MAC

TIGER Phase 2




Status: AL 59/Markings

Engineer: Volkert

Contractor: A&B



TIGER Phase 3

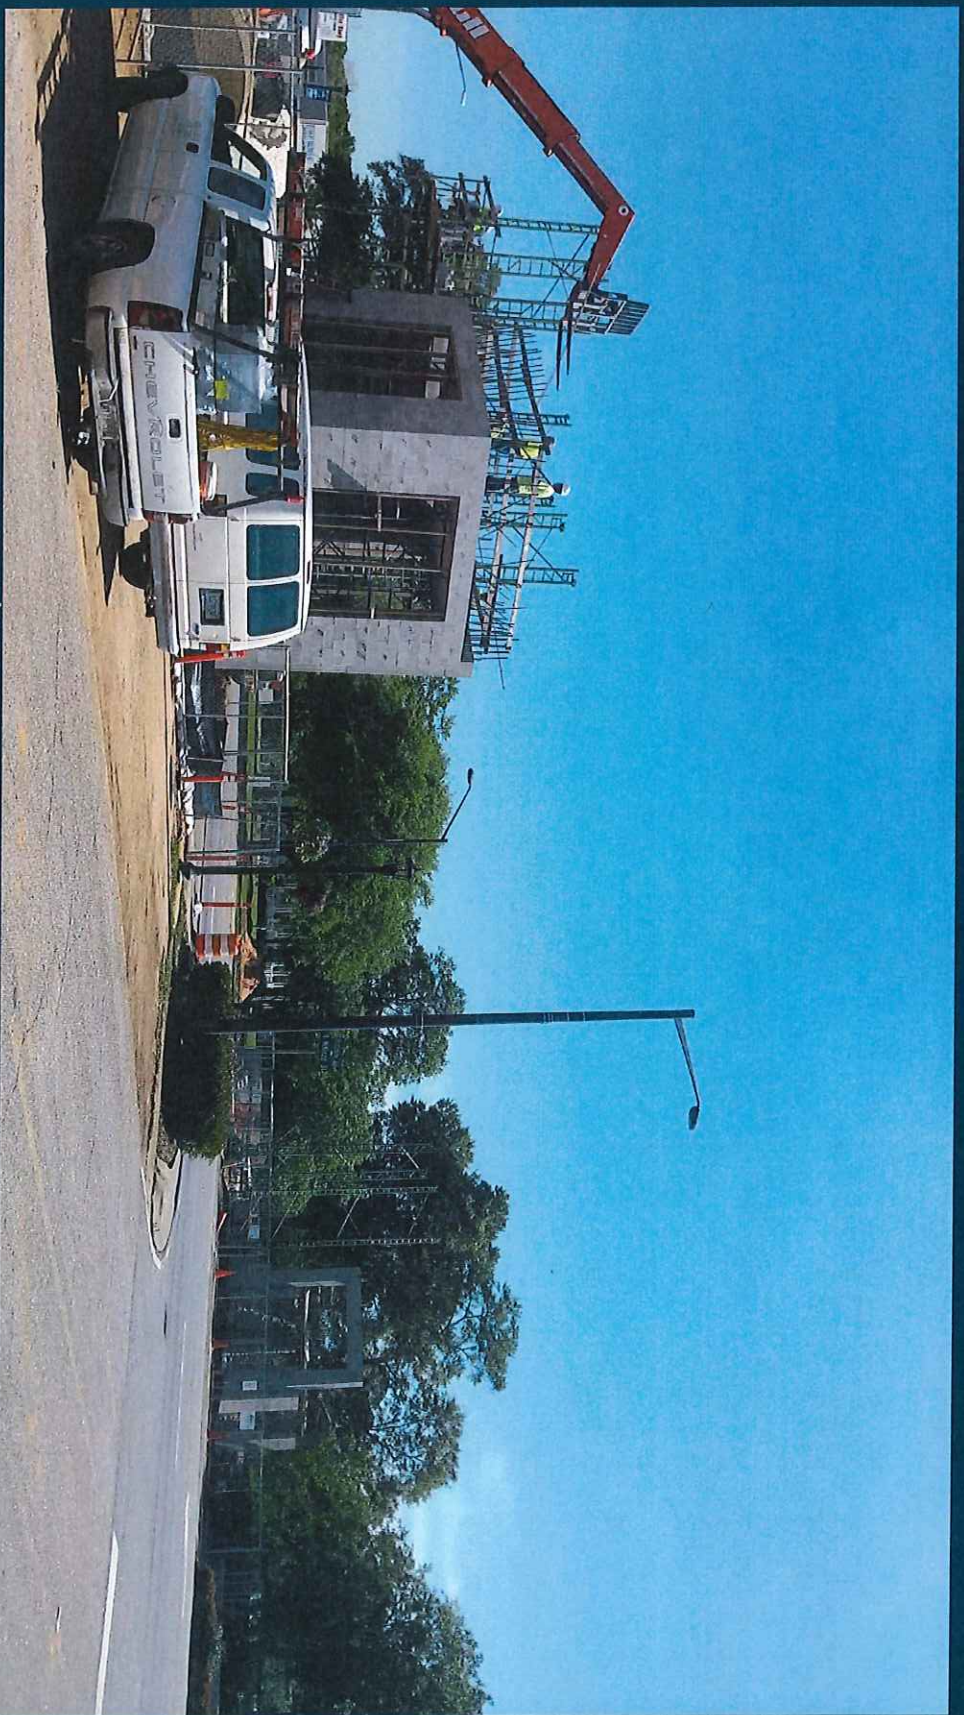

Status: Block

Engineer: Volkert

Contractor: Morette

Violet Avenue Pipe Replacement



Status: Complete

Engineer: COF

Contractor: Public Works

QUESTIONS?

